



## CUT PERMIT

**Description:** Contractor shall saw cut existing pavement, install waterline or sewer line and backfill according to the standard drawing (see attached). Once Contractor is ready to re-pave trench, the Contractor shall saw cut 12” on both sides of the open trench. A compaction test is required at 95% compaction. After the compaction test is verified by a City Employee, the Contractor shall install 3” minimum asphalt patch. Contractor shall then use the straight edge method to verify no more than 1/4” gap in the space of 10 feet. All trenches must be maintained until asphalt is replaced. Replacement shall occur within 10 days of cut, or at the discretion of the Public Works Director.

**When permit is required:** A Cut Permit is required any time an individual or company plans to cut a roadway within the Preston City Limits.

**Name of property owner:** \_\_\_\_\_

**Name of contractor:** \_\_\_\_\_

**Address of property:** \_\_\_\_\_


**Reason to cut pavement:** \_\_\_\_\_

**Agency Conducting Compaction Test:** \_\_\_\_\_

**Date Permit Granted:** \_\_\_\_\_

\_\_\_\_\_  
**Signature of Inspecting City Employee**

\_\_\_\_\_  
**Date Inspection Completed**

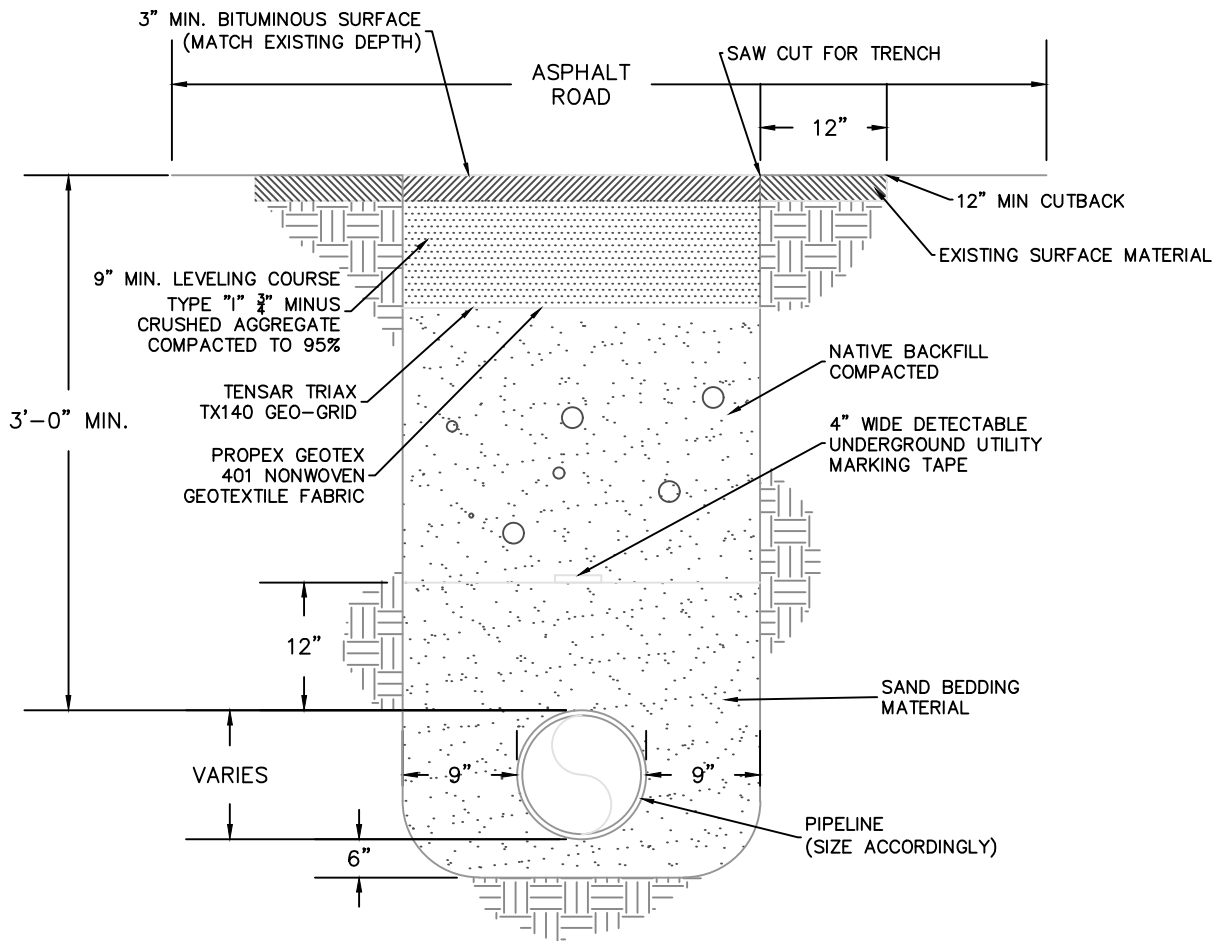

**NOTES:**

1. TRENCH DETAILS INSIDE OF ASPHALT ROADS.
2. ASPHALT ROADS SHALL BE SAW CUT.

A
TYP
**DETAIL - PAVED ROADWAY TRENCH**  
 N.T.S.
